



## North Bank Playground

Completed By: Patrick McCord

Date of Report: February 19, 2020

Time of Observation: 1:00 PM

| EATHER  |   |                   |                   |                   |              |                   |              |
|---|---|-------------------|-------------------|-------------------|--------------|-------------------|--------------|
|   | Clear   | PM                | Calm              |                   | <10 deg      |                   | 61-70 deg    |
| PM  | P/Cloudy  |                   | Slight Breeze     |                   | 11-20 deg    |                   | 70-80 deg    |
|   | Overcast  |                   | Moderate Winds    |                   | 21-32 deg    |                   | 80-90 deg    |
|   | Rain  |                   | Windy             | PM                | 33-45 deg    |                   | 91-99 deg    |
|   | Smokey  |                   | Very Windy +35mph |                   | 45-60 deg    |                   | 100+         |
|   | Snow  |                   |                   |                   |              |                   |              |
| 2. CONSTRUCTION ACTIVITY  |   |                   |                   |                   |              |                   |              |
| Area  | Observation   |                   |                   |                   |              |                   |              |
| Site  | Site layout being done.<br>Roof shingles being removed at large shelter.<br>Building demolition is 98% complete; debris being sorted.<br>Additional boulders have been unloaded at the existing pile. |                   |                   |                   |              |                   |              |
| Building  |   |                   |                   |                   |              |                   |              |
| 3. LABOR (REPORTED FROM GENERAL CONTRACTOR)   |   |                   |                   |                   |              |                   |              |
| Contractor  | # Of Workers  | Contractor        | # Of Workers      | Contractor        | # Of Workers | Contractor        | # Of Workers |
| T LaRiviere   | 6   |                   | 0                 |                   | 0            |                   | 0            |
|   |   |                   |                   |                   |              |                   |              |
| 4. EQUIPMENT ON SITE  |   |                   |                   |                   |              |                   |              |
| Type of Equipment   | #   | Type of Equipment | #                 | Type of Equipment | #            | Type of Equipment | #            |
| Compaction roller   | 0   | Dozer             | 0                 | Track hoe         | 4            |                   |              |
| Mini excavator  | 0   | Front loader      | 0                 | Water truck       | 0            |                   |              |
| Bobcat  | 1   | Extended forklift | 1                 | Side dump truck   | 0            |                   |              |
| Man lift  | 0   |                   |                   |                   |              |                   |              |
| 5. TPZ  |   |                   |                   |                   |              |                   |              |
| <ul style="list-style-type: none"><li>Fencing is installed at existing trees</li></ul>        |   |                   |                   |                   |              |                   |              |
| 6. DELIVERIES & CONDITIONS Note time and type of delivery                                     |   |                   |                   |                   |              |                   |              |
| <ul style="list-style-type: none"><li></li></ul>  |   |                   |                   |                   |              |                   |              |
| 7. FIELD DISCUSSIONS OR NOTES (provide bulleted list of discussions, directions or decisions) |   |                   |                   |                   |              |                   |              |
| <ul style="list-style-type: none"><li></li></ul>  |   |                   |                   |                   |              |                   |              |
| 8. SCHEDULE REVIEW  |   |                   |                   |                   |              |                   |              |
| <ul style="list-style-type: none"><li></li></ul>  |   |                   |                   |                   |              |                   |              |
| 9. PROJECT PHOTOGRAPHS  |   |                   |                   |                   |              |                   |              |
| <ul style="list-style-type: none"><li>See pictures below:</li></ul>                           |   |                   |                   |                   |              |                   |              |



## North Bank Playground

Completed By: Patrick McCord

Date of Report: February 19, 2020

Time of Observation: 1:00 PM


---



#1 View from cliff (facing southeast)



#2 Remaining stockpile adjacent to the west ramp.

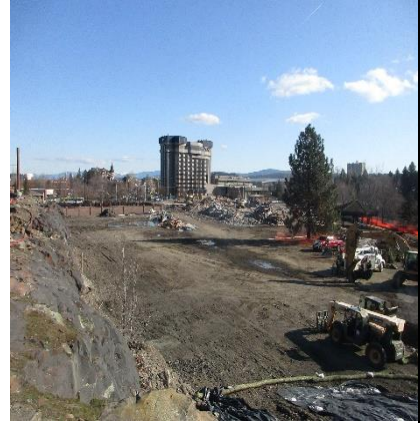

#3 View from cliff (facing east)



#4 Tree protection zone.



#5 Roof shingle removal at shelter.



#6 Debris being sorted.



# 7 View from southeast corner (facing west).



#8 View from northeast corner facing south (at the intersection).



#9 View from the cliff (facing south)
