



## North Bank Playground

Completed By: Patrick McCord

Date of Report: December 10, 2020

Time of Observation: 11:30 AM

1. WEATHER							
	Clear	AM	Calm		<10 deg		61-70 deg
	P/Cloudy		Slight Breeze		11-20 deg		70-80 deg
AM	Overcast		Moderate Winds		21-32 deg		80-90 deg
	Rain		Windy	AM	33-45 deg		91-99 deg
	Smokey		Very Windy +35mph		45-60 deg		100+
	Snow						
2. CONSTRUCTION ACTIVITY							
Area	Observation						
Site	Brick pavers have been installed at south side of basketball court. Topsoil being placed at swales. Splash pad conduits being installed. Parking lot curbs being formed. Play Tower panels being installed. Roof underlayment has been installed on the small shelter. Bench footings being formed.						
Building	1 <sup>st</sup> floor wall insulation being installed. Interior 1 <sup>st</sup> floor walls being taped and finished. West canopy steel decking has been installed. Exterior soffit insulation being installed. Tile being installed in Restrooms.						
3. LABOR							
Contractor	# Of Workers	Contractor	# Of Workers	Contractor	# Of Workers		
T LaRiviere	23	Colvico	4	Road Products	0		
Air Tech Mechanical	0	Ascent Plumbing	0	NW Playground	4		
Drywall Specialties	5	Tile	2				
4. EQUIPMENT ON SITE							
Type of Equipment	#	Type of Equipment	#	Type of Equipment	#		
Compaction roller	1	Grader	0	Track hoe	0		
Dozer	1	Front loader	1	Water truck	1		
Bobcat	3	Extended forklift	1	Manlifts	2		
Backhoe	1	Mini excavator	2	Extended manlift	2		
5. TPZ							
•							
6. DELIVERIES & CONDITIONS Note time and type of delivery							
•							
7. FIELD DISCUSSIONS OR NOTES (provide bulleted list of discussions, directions or decisions)							
•							
8. SCHEDULE REVIEW							
•							
9. PROJECT PHOTOGRAPHS							



## North Bank Playground

Completed By: Patrick McCord

Date of Report: December 10, 2020


Time of Observation: 11:30 AM



#1 O&M Building (view from southwest corner).



#2 O&M Building (view from southeast corner).

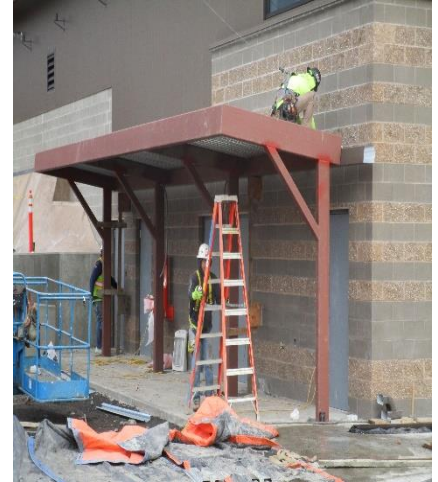

#3 West side M&O canopy.



#4 Thermal insulation at 1<sup>st</sup> floor walls.



#5 Splash pad rough-in..



#6 Staining at concrete knee walls.



#7 Play Tower installation.



#8 Sidewalk installation(east side of BB court).



#9. Brick pavers at south side of BB court.
