Qwuloolt Update 3.20.13.xml

20-Mar-13 10:56

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
Qwuloolt Update 3.20.13.xml		0	0		
Milestones		5	0	10-Oct-12 A	11-Oct-12 A
CLIN 01		5	0	10-Oct-12 A	11-Oct-12 A
A1000	Project Preconstruction Meeting	1	0	10-Oct-12 A	10-Oct-12 A
A6010	Start Phase (NTP)	0	0	10-Oct-12 A	
A6130	Bond	5	0	10-Oct-12 A	11-Oct-12 A
Submittals		146	40	17-Oct-12 A	14-May-13
CLIN 01		107	1	17-Oct-12 A	20-Mar-13
S1000	Sub Progress Charts	12	0	17-Oct-12 A	30-Oct-12 A
S1010	Sub Employee Listing	12	0	17-Oct-12 A	02-Nov-12 A
S1020	Sub Project Schedule	12	0	17-Oct-12 A	30-Oct-12 A
S1030	Sub Submittal Register	12	0	17-Oct-12 A	10-Jan-13 A
S1040	Sub Accident Prevention Plan	12	0	17-Oct-12 A	24-Oct-12 A
S1050	Sub Quality Control Plan	12	0	17-Oct-12 A	19-Oct-12 A
S1060	Sub Original Site Photos	0	0	17-Oct-12 A	20-Mar-13
S1080	Sub EPP	20	0	17-Oct-12 A	04-Jan-13 A
S1100	Sub SWPPP	20	0	17-Oct-12 A	02-Jan-13 A
S1110	Sub Storm Water NOI	20	0	17-Oct-12 A	04-Jan-13 A
S1120	Sub 31 00 00 - EarthWork	20	0	17-Oct-12 A	17-Jan-13 A
S1130	Sub 31 05 19 - Geotextile	20	0	17-Oct-12 A	13-Nov-12 A
S1140	Sub31 05 21 - Geogrid	20	0	17-Oct-12 A	13-Nov-12 A
S1150	Sub 32 11 23 - Aggregate Base	20	0	17-Oct-12 A	13-Dec-12 A
S1200	Sub 35 41 00 - Levee Construction	20	0	17-Oct-12 A	18-Dec-12 A
SA2050	App Quality Control Plan	11	0	19-Oct-12 A	19-Nov-12 A
SA2040	App Accident Prevention Plan	11	0	24-Oct-12 A	20-Dec-12 A
SA2000	App Progress Charts	11	0	30-Oct-12 A	08-Jan-13 A
SA2020	App Prelimenary Project Schedule	11	0	30-Oct-12 A	02-Jan-13 A
SA2010	App Employee Listing	11	0	02-Nov-12 A	05-Nov-12 A
SA2130	App 31 05 19 - Geotextile	0	0	13-Nov-12 A	14-Nov-12 A
SA2140	App 31 05 21 - Geogrid	20	0	13-Nov-12 A	20-Mar-13
SA2150	App 32 11 23 - Aggregate Base	20	0	13-Dec-12 A	15-Jan-13 A
SA2200	App 35 41 00 - Levee Construction	20	0	18-Dec-12 A	15-Jan-13 A
SA2100	App SWPPP	11	0	02-Jan-13 A	28-Jan-13 A
SA2080	App EPP	11	0	04-Jan-13 A	22-Jan-13 A
SA2110	App Storm Water NOI	11	0	04-Jan-13 A	08-Jan-13 A
SA2030	App Submittal Register	11	0	10-Jan-13 A	14-Jan-13 A
SA2060	App Original Site Photos	1	1	20-Mar-13	20-Mar-13
CLIN 02		146	40	17-Oct-12 A	14-May-13
S1070	Sub Diversion & Water Plan	20	20	17-Oct-12 A	16-Apr-13
S1090	Sub Water Quality Plan	20	20	17-Oct-12 A	16-Apr-13
S1160	Sub 32 15 00 Crushed Surface Course	20	0	17-Oct-12 A	13-Dec-12 A
SA2120	App 31 00 00 - EarthWork	20	0	17-Jan-13 A	28-Feb-13 A
S1170	Sub 32 92 19 - Seeding	20	20	20-Mar-13	16-Apr-13
S1180	Sub 33 40 00 Storm Drainage	20	20	20-Mar-13	16-Apr-13

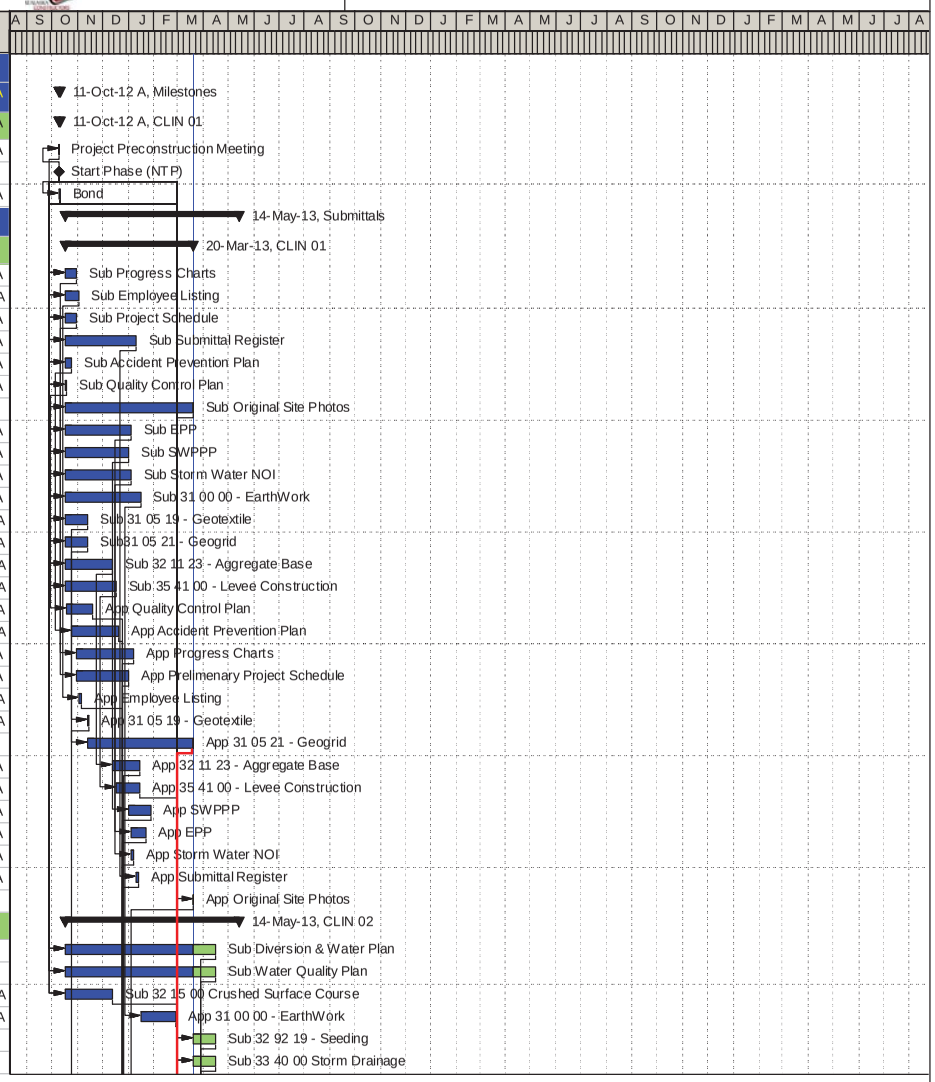

Actual Work | Critical Remaining Work | Summary | Remaining Work | Milestone

Date	Revision	Checked	Approved

You created this PDF from an application that is not licensed to print to novaPDF printer (http://www.novapdf.com)

Qwuloolt Update 3.20.13.xml

20-Mar-13 10:56

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
S1190	Sub 35 31 19 - Stone Slope	20	20	20-Mar-13	16-Apr-13
S1210	Sub 03 20 00.00 10 Conc Reinforce	20	20	20-Mar-13	16-Apr-13
S1220	Sub 03 30 53 - Cast-in-Place	20	20	20-Mar-13	16-Apr-13
S1230	Sub 03 40 00.00.10 Plant-Precast	20	20	20-Mar-13	16-Apr-13
SA2160	App 32 15 00 Crushed Surface Course	20	20	20-Mar-13	16-Apr-13
SA2070	App Diversion water care Plan	11	11	17-Apr-13	01-May-13
SA2090	App Water Quality Monitoring Plan	11	11	17-Apr-13	01-May-13
SA2170	App 32 92 19 - Seeding	20	20	17-Apr-13	14-May-13
SA2180	App 33 40 00 Storm Drainage	20	20	17-Apr-13	14-May-13
SA2190	App 35 31 19 - Stone Slope Protection	20	20	17-Apr-13	14-May-13
SA2210	App 3 20 00.00 10 Concrete Reinforce	20	20	17-Apr-13	14-May-13
SA2220	App 03 30 53 - Cast-in-Place Conc	20	20	17-Apr-13	14-May-13
SA2230	App 03 40 00.00.10 Plant-Precast	20	20	17-Apr-13	14-May-13
Procurement		79	45	13-Nov-12 A	21-May-13
CLIN 01		59	25	13-Nov-12 A	23-Apr-13
FAB3010	Fab 31 05 19 - Geotextile	5	5	13-Nov-12 A	26-Mar-13
FAB3030	Fab 32 11 23 - Aggregate Base	5	0	15-Jan-13 A	16-Jan-13 A
FAB3020	Fab 31 05 21 - Geogrid	25	25	20-Mar-13	23-Apr-13
CLIN 02		45	45	20-Mar-13	21-May-13
FAB3000	Fab 31 00 00 - EarthWork	5	5	20-Mar-13	26-Mar-13
FAB3080	Fab 35 41 00 - Levee Construction	5	5	20-Mar-13	26-Mar-13
FAB3040	Fab 32 15 00 Crushed Surface Course	5	5	17-Apr-13	23-Apr-13
FAB3050	Fab 32 92 19 - Seeding	5	5	15-May-13	21-May-13
FAB3060	Fab 33 40 00 Storm Drainage	5	5	15-May-13	21-May-13
FAB3070	Fab 35 31 19 - Stone Slope Protection	5	5	15-May-13	21-May-13
FAB3090	Fab 3 20 00.00 10 Concrete Reinforce	5	5	15-May-13	21-May-13
FAB3100	Fab 03 30 53 - Cast-in-Place Conc	5	5	15-May-13	21-May-13
FAB3110	Fab 03 40 00.00.10 Plant-Precast	5	5	15-May-13	21-May-13
Construction		491	418	14-Jan-13 A	28-Nov-14
CLIN 01		391	318	14-Jan-13 A	11-Jul-14
A5030	Mobilization	10	0	14-Jan-13 A	16-Jan-13 A
A5040	Installation of TESC	5	0	24-Jan-13 A	31-Jan-13 A
A5060	Stripping	30	30	16-Apr-13*	28-May-13
A5070	Foundation Preperation	29	29	24-Apr-13	04-Jun-13
A5080	Access Road Construction	29	29	01-May-13	11-Jun-13
A5100	Install Piezometers	9	9	15-May-13	28-May-13
A5110	Install Inclinometer	9	9	15-May-13	28-May-13
A5120	Install Monitoring Plates	9	9	15-May-13	28-May-13
A5091	Levee Lift #1 STA 20+00-0+00	18	18	29-May-13	21-Jun-13
A5092	Levee Lift #2 STA 20+00-0+00	13	13	24-Jun-13	11-Jul-13
A5093	Levee Lift #1 StA 20+00-39+00	24	24	12-Jul-13	14-Aug-13
A5050	Installation of Dewatering	5	5	25-Jul-13	31-Jul-13
A5094	Levee Lift #2 STA 20+00-39+00	16	16	15-Aug-13	06-Sep-13
A5095	Levee Lift #3 STA 20+00	7	7	09-Sep-13	17-Sep-13
A5096	Levee Lift # 3 STA 20+00-39+00	10	10	18-Sep-13	01-Oct-13

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

Date	Revision	Checked	Approved

You created this PDF from an application that is not licensed to print to novaPDF printer (http://www.novapdf.com)

Qwuloolt Update 3.20.13.xml

20-Mar-13 10:56

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
A5150	Slope Stablization	2	2	02-Oct-13	03-Oct-13
A5165	Surcharge Period	200	200	02-Oct-13	11-Jul-14
A5160	Demobilize Year one	1	1	04-Oct-13	04-Oct-13
CLIN 02		103	103	09-Jul-14	28-Nov-14
A5162	Remobilize Year 2	3	3	09-Jul-14	11-Jul-14
A5180	Levee Final Grading	38	38	14-Jul-14	03-Sep-14
A5097	Build North/South Draingage Ditch	5	5	14-Jul-14	18-Jul-14
A5220	Levee Filter Rock	7	7	04-Sep-14	12-Sep-14
A5230	Levee RipRap	20	20	15-Sep-14	10-Oct-14
A5190	Installation of Storm Culvert	10	10	25-Sep-14	08-Oct-14
A5250	Levee Topsoil	1	1	11-Nov-14	11-Nov-14
A5260	Levee Access Road Gravel	5	5	12-Nov-14	18-Nov-14
A5270	Demobilization	5	5	19-Nov-14	25-Nov-14
A5300	Hydroseed.Revegetation	3	3	26-Nov-14	28-Nov-14
CLIN 04		21	21	13-Oct-14	10-Nov-14
A5240	Levee Breech	21	21	13-Oct-14	10-Nov-14
Closeout		34	34	28-Nov-14	15-Jan-15
CLIN 02		34	34	28-Nov-14	15-Jan-15
A6140	Substantial Completion	0	0		28-Nov-14
A6000	Submit and Approval of O&M	5	5	05-Dec-14	11-Dec-14
A6080	Contractor's Pre-Final Inspection	2	2	25-Dec-14	26-Dec-14
A6090	Punchlist from Contractor	5	5	29-Dec-14	02-Jan-15
A6100	Gov't Pre-final inspection	3	3	05-Jan-15	07-Jan-15
A6110	Punchlist from Gov't	5	5	08-Jan-15	14-Jan-15
A6120	Final Inspection	1	1	15-Jan-15	15-Jan-15
CLIN 03		9	9	12-Dec-14	24-Dec-14
A6070	Submit and Approval of As-Built	9	9	12-Dec-14	24-Dec-14

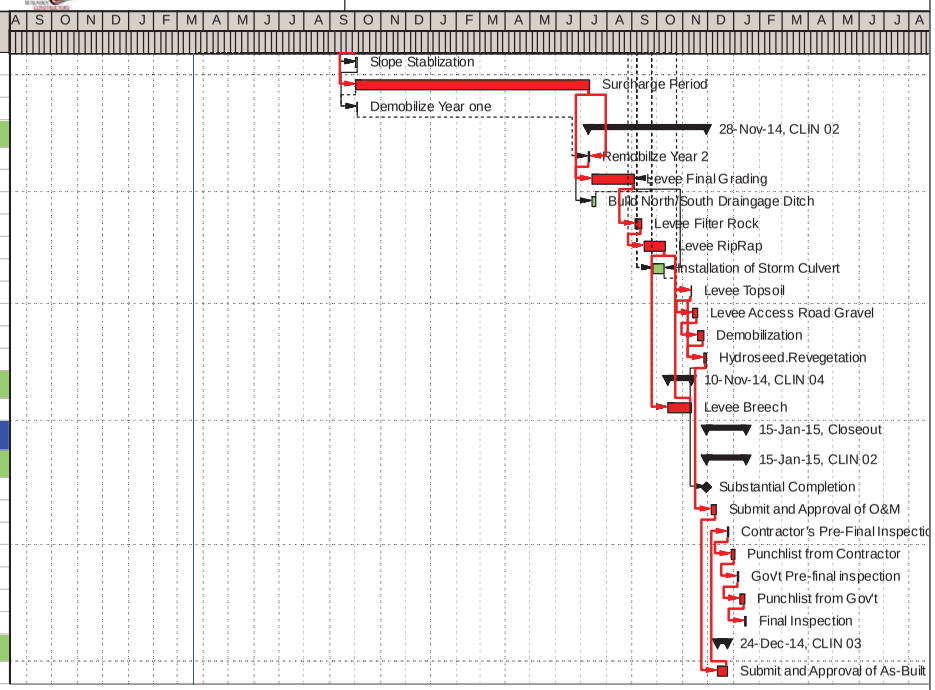

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

Date	Revision	Checked	Approved

You created this PDF from an application that is not licensed to print to novaPDF printer (http://www.novapdf.com)
